PLAINTIFF'S
EXHIBIT
UC-1091

MEMORANDUM

PLANT ASBESTOS PROJECT

By

J. F. Schultz

Union Carbide Corporation

Texas City Plant

July 19, 1985

Union Carbide trial exhibit UC-1091: J. F. Schultz, Plant Asbestos Project Memorandum on Asbestos Insulation Re… Published by AsbestosClaims.Law
ACL Doc 16275 · Page 1 of 18 asbestosclaims.law/library/16275/1

Table of Contents

1. Foreward..... 1
2. Introduction..... 2
3. Summary..... 3
4. Recommendations..... 6
5. Discussion..... 9
6. Housekeeping..... 11
7. Asbestos Identification..... 11
8. Acknowledgement..... 12
9. Appendix
   Cost Estimate
   Identification of Piperack Priorities

UCTC 06789

FOREWARD

The Texas City Plant is concerned about the potential health hazards of asbestos. Accordingly, development of an action plan addressing this concern was authorized. The primary objectives of the action plan are:

1. To ascertain the magnitude of asbestos insulation requiring repair and which therefore presents a potential for release of asbestos fibers to the environment.
2. To recommend corrective action which will eliminate, in-so-far as possible, asbestos contamination of the environment.

Union Carbide trial exhibit UC-1091: J. F. Schultz, Plant Asbestos Project Memorandum on Asbestos Insulation Re… Published by AsbestosClaims.Law
ACL Doc 16275 · Page 3 of 18 asbestosclaims.law/library/16275/3

INTRODUCTION

An assessment of the amount of exposed "asbestos suspect" insulation was completed for the entire plant (exclusive of office buildings, control rooms, laboratories and shops). This assessment was accomplished through site surveys performed by inspection teams appointed by the department heads. Valuable assistance was given these teams by hourly insulator craftsmen and leadmen and Industrial Hygiene departmental personnel. Cost estimates in the ±30% range were made by the plant insulator group.

Union Carbide trial exhibit UC-1091: J. F. Schultz, Plant Asbestos Project Memorandum on Asbestos Insulation Re... Published by AsbestosClaims.Law
ACL Doc 16275 · Page 4 of 18 asbestosclaims.law/library/16275/4

SUMMARY

Due to the weathered condition and to some degree damage to the insulation weather barrier, and to the insulation itself, significant amounts of exposed "asbestos suspect" insulation exists in the plant.

Estimates of the quantity of asbestos suspect insulation requiring repair together with a cost estimate for correcting the exposed or damaged areas are tabulated below. The arrangement of the tabulation also prioritizes the problem areas in descending order.

Union Carbide trial exhibit UC-1091: J. F. Schultz, Plant Asbestos Project Memorandum on Asbestos Insulation Re… Published by AsbestosClaims.Law
ACL Doc 16275 · Page 5 of 18 asbestosclaims.law/library/16275/5

Priority	Location	Estimated Insulation Repair Required Equipment(ft^2)	Piping(Lin.ft)	Estimated Cost M$
1.	No. 2 Olefins	12,500	11,100	325.0
2.	Phenolic Resins (B-176) and Solvent Resins Piperack	240	2,210	56.4
3.	Bldg. 45	400	2,220	155.7
4.	Acids & Esters			
	Bldg. 17	minor		
	Bldg. 21 and 24	2,818	690	80.2
	Bldg. 54	none	305	
5.	No. 3 Olefins	2,280	12,764	465.2
6.	Plant Piperacks	none	16,171	402.4
7.	OXO			
	OXO Syn Gas (B-139 etc.)		3,410	
	Bldg. 79		189	47.0
	Bldg. 83		530	
8.	E. O. D.			
	Bldg. 51	minor	720	20.6
	Bldg. 219	700	3,300	65.7
9.	Ethanol & DES	minor	1,420	47.2
10.	No.1 Steam Plant		719	68.2
	No.3 Steam Plant	140	295	18.2
11.	In-plant Distribution	none	1,233	26.2
12.	Pump Houses			
	#4		105	
	#6		35	13.1
	#7		27	
			Grand Total	1791.1

UCTC 06793

The critera used when prioritizing the potential asbestos problem areas are as follows:

1. Potential exposure of asbestos to plant personnel.
2. Potential for contaminating the community.
3. Exposed insulation which is highly visible and easily seen by the casual observer.

Union Carbide trial exhibit UC-1091: J. F. Schultz, Plant Asbestos Project Memorandum on Asbestos Insulation Re... Published by AsbestosClaims.Law
ACL Doc 16275 · Page 7 of 18 asbestosclaims.law/library/16275/7

RECOMMENDATIONS

The overall action plan recommended is as follows:

1. As soon as possible (this year if possible) begin to correct the exposed asbestos containing insulation by, removing or covering the insulation using metal or mastic weather barriers at these "high priority" locations:

    a. No. 2 Olefins

        1) The Firebird, exhaust duct, and Waste Heat Boiler. Action: Remove.

        2) The three columns and associated equipment from the old butadiene (vinyl acetate and acetone recovery) unit. Action: Remove

        3) Flue gas breeching, cracking furnaces at building 105. Action: Remove.

        4) Dead 1 1/2" and 2" acetylene lines in 5th Street piperack. Action: Remove.

        5) Exhaust mufflers in building 103. Action: Mastic Coat.

        6) Pipelines where the insulation is intact but weather barrier has deteriorated. Action: Mastic Coat.

UCTC 06795

b. Phenolic Resin Unit - Building 176

1) Tanks and piping. Action: Remove.

2) No. 70 Column Flask Tank. Action: Remove.

3) Pipelines in piperack between buildings 122 and 176. Action: "Metal out" and/or Mastic Coat.

c. Building 45 Hydrogen Converters.

1) No. 3, 4, and 5 Hydrogenators. Action: Remove asbestos and re-insulate with non-asbestos.

2) No. 1 and 2 Hydrogenators. Action: Install metal weather barrier.

3) Piping. Action: Use metal or mastic weather barrier where insulation in intact.

d. Building 24.

1) Acid Still Fore column. Action: Remove.

2) Acid Still. Action: Remove.

3) Acid Refining Column. Action: Remove.

4) No. 2 Esters Refining Still. Action: Remove asbestos insulation and replace with non-asbestos.

5) Condensate Tank. Action: Remove asbestos insulation and replace with non-asbestos.

6) 4: Dead Oxide Line. Action: Remove.

Union Carbide trial exhibit UC-1091: J. F. Schultz, Plant Asbestos Project Memorandum on Asbestos Insulation Re... Published by AsbestosClaims.Law
ACL Doc 16275 · Page 9 of 18 asbestosclaims.law/library/16275/9

2. Each department including those not listed above will work out an action plan to correct the problem areas in their respective departments using the asbestos suspect survey data obtained by the inspection teams. The magnitude of the corrective work required for the entire plant precludes completion in one year. However department action plans should target for completion within a 2 to 4 year period.
3. Each department will include in their 1986 budget preparations funds for correcting their most obvious and/or greatest exposure potential areas.
4. Subsequent years budgets to include funds until resolution of the problem areas is completed.

Union Carbide trial exhibit UC-1091: J. F. Schultz, Plant Asbestos Project Memorandum on Asbestos Insulation R... Published by AsbestosClaims.Law
ACL Doc 16275 · Page 10 of 18 asbestosclaims.law/library/16275/10

DISCUSSION

Included in the appendix of this report is a tabulation of cost estimates for the various departments. These cost estimates were developed by the plant insulator group and have a ±30% accuracy.

When planning repairs to the exposed asbestos insulation, the following guidelines are suggested.

1. Determine whether or not the insulation contains asbestos. If the insulation does not contain asbestos fibers, a decision to defer repair should be made. Economic considerations (energy conservation, production restraints, etc.) or safety considerations may result in a decision to go ahead with the repair anyway.
2. If the asbestos containing insulation is in poor condition (hanging loose, broken up, sagging, etc.), remove the old insulation and replace with asbestos free material.
3. If the weather barrier is in poor condition (or essentially gone), but the insulation itself is in fairly good condition:
   a) Fill up the voids or breaks with non-asbestos filler if necessary.
   b) Cover straight runs of piping with metal and/or mastic weather barrier.
   c) "Mastic in" valves, 90° elbows, and other non-uniform sections.
   d) Use a combination of metal or mastic weather barrier or columns and other equipment.
4. If the weather barrier has breaks, is damaged, or missing over short reactions repair using a generous coating of mastic.

Union Carbide trial exhibit UC-1091: J. F. Schultz, Plant Asbestos Project Memorandum on Asbestos Insulation R... Published by AsbestosClaims.Law
ACL Doc 16275 · Page 11 of 18 asbestosclaims.law/library/16275/11

5. If the insulation has "end or "edge" exposure, generously coat these exposed areas with an approved mastic. This treatment should be considered where "dead" or out-of-service piping or equipment has insulation which needs to be repaired.
6. If the asbestos containing insulation is in poor condition and is installed on "dead lines" or out-of-service equipment, remove and dispose this insulation.
7. Reference to the "Remarks" column of the inspection data sheets (Main Piperack Survey, Unit Equipment Survey, or Unit Piping Survey data sheets) will generally include comments on suggested repair.
8. Seek advice from the plant insulator group as required.

Union Carbide trial exhibit UC-1091: J. F. Schultz, Plant Asbestos Project Memorandum on Asbestos Insulation R... Published by AsbestosClaims.Law
ACL Doc 16275 · Page 12 of 18 **asbestosclaims.law/library/16275/12**

HOUSEKEEPING

The entire plant places itself in a position of being open for censure from regulatory agencies when loose insulation is allowed to lie on the ground or has been left where it has fallen from equipment, piping, etc. Picking up and removing this insulation for disposal should be done on a continuing basis.

ASBESTOS IDENTIFICATION

Distinctive warning identification such as yellow adhesive backed film with black lettering is recommended for identifying asbestos containing insulation on equipment and pipe lines.

Pipelines in piperacks should be thusly identified approximately every 100 - 150 feet.

Union Carbide trial exhibit UC-1091: J. F. Schultz, Plant Asbestos Project Memorandum on Asbestos Insulation R... Published by AsbestosClaims.Law
ACL Doc 16275 · Page 13 of 18 **asbestosclaims.law/library/16275/13**

ACKNOWLEDGEMENT

The response by the plant to the request for "walk through inspections" of the operating areas and the plant piperacks was outstanding. Suitable recognition of everyone who participated may be impossible. However, recognition of the following for their commendable support and effort is in order because without their help this project could not have gotten off the ground.

DEPARTMENT	INDIVIDUALS
Energy Systems	W. D. (Bill) Wilkins W. N. Parker R. A. Rivera C. R. Malveaux O. B. Hayden
Ethylene Oxide Derivatives	T. F. Hanrahan
No. 2 Olefins	T. W. Cates Henry G. Parker
Ethanol and DES	F. G. McWhorter J. A. McKenzie
Solvents and Acids	Frank L. Campbell J. L. Lamb J. B. Richards
In-Plant Distribution	J. L. Pedraza B. C. Wedhorn

Union Carbide trial exhibit UC-1091: J. F. Schultz, Plant Asbestos Project Memorandum on Asbestos Insulation R... Published by AsbestosClaims.Law
ACL Doc 16275 · Page 14 of 18 asbestosclaims.law/library/16275/14

DEPARTMENT	INDIVIDUALS
Solvent Vinyls	D. B. Rygaard W. E. Benskin R. F. Garza R. J. Hadley R. Hernandez H. Martinez B. L. Nall J. Nunez E. K. Sumrall
Vinyl Acetate	Donald R. Kirkland
No. 3 Olefins	N. Dean Sharp Roy M Hughes O. T. Mallett Angel Echevarria
OXO and OXO Syn Gas	Marcie Laundrie Dan O'Neil J. D. Duston L. M Gonzalez
Industrial Hygiene	Kirk E. Martin C. W. Perry D. W. Harkreader

Also, the support and assistance received from the Insulator Craft group was outstanding. Special thanks and appreciation is due these people:

J. E. Barnes
H. P. Smith
H. G. Kelly Jr.
Keye Harding
D. R. Labry
P. J. Bartlett

Union Carbide trial exhibit UC-1091: J. F. Schultz, Plant Asbestos Project Memorandum on Asbestos Insulation R... Published by AsbestosClaims.Law
ACL Doc 16275 · Page 15 of 18 **asbestosclaims.law/library/16275/15**

Union Carbide trial exhibit UC-1091: J. F. Schultz, Plant Asbestos Project Memorandum on Asbestos Insulation R...
ACL Doc 16275 · Page 16 of 18
Published by AsbestosClaims.Law
asbestosclaims.law/library/16275/16

COST ESTIMATES

PLANT ASBESTOS PROJECT


July 19. 1985

DEPARTMENT	AREAS INVOLVED	MATERIAL M$	INSULATOR LABOR M$	SUBTOTAL M$	MISC AND ESCALATION M$	TOTAL M$
Energy Systems	Main Piperack	23.9	285.7	309.6	92.8	402.4
	No.1 Steam Plant	8.0	46.3	54.3	13.9	68.2
	No.3 Steam Plant	1.3	13.0	14.3	3.9	18.2
	Pump Houses	1.5	8.6	10.1	3.0	13.1
E. O. D.	Bldg. 51	1.0	15.1	16.1	4.5	20.6
	Bldg. 219	2.0	49.0	51.0	14.7	65.7
No.2 Olefins		18.0	236.2	254.2	70.8	325.0
Ethanol-D.E.S.	Bldg. 15	1.8	15.4	17.2	4.6	21.8
	Bldg. 94	2.2	17.9	20.1	5.3	25.4
Solvents and Acids	Bldg. 17	1.9	26.7	28.6	8.0	36.6
	Bldg. 21	--	1.5	1.5	0.5	2.0
	Bldg. 24	0.4	20.9	21.3	6.3	27.6
	Bldg. 54	0.4	10.4	10.8	3.2	14.0
In-Plant Distribution	Bldg. 19	9.7	12.5	22.2	4.0	26.2
Solvent Vinyls	Bldg.176 & P/R	2.4	41.5	43.9	12.5	56.4
Vinyl Acetate	Bldg.110 & 111	none	none	none	none	none
No. 3 Olefins		24.7	338.5	363.2	102.0	465.2
OXO-Syn Gas	Bldg. 45	3.0	66.7	69.7	20.0	89.7
	Bldg.45 Converters	9.3	43.6	52.9	13.1	66.0
	Bldg. 79	0.5	6.9	7.4	2.1	9.5
	Bldg. 83	0.5	14.9	15.4	4.5	19.9
	Bldg.282 (Syn Gas)	0.5	13.1	13.6	4.0	17.6
	GRAND TOTALS	113.0	1,284.4	1,397.4	393.7	1,791.1

(1) Escalated labor cost by 30% for scaffolding, asbestos disposal and contingancies.

UCTC 06803

Identification of Piperack Priorities

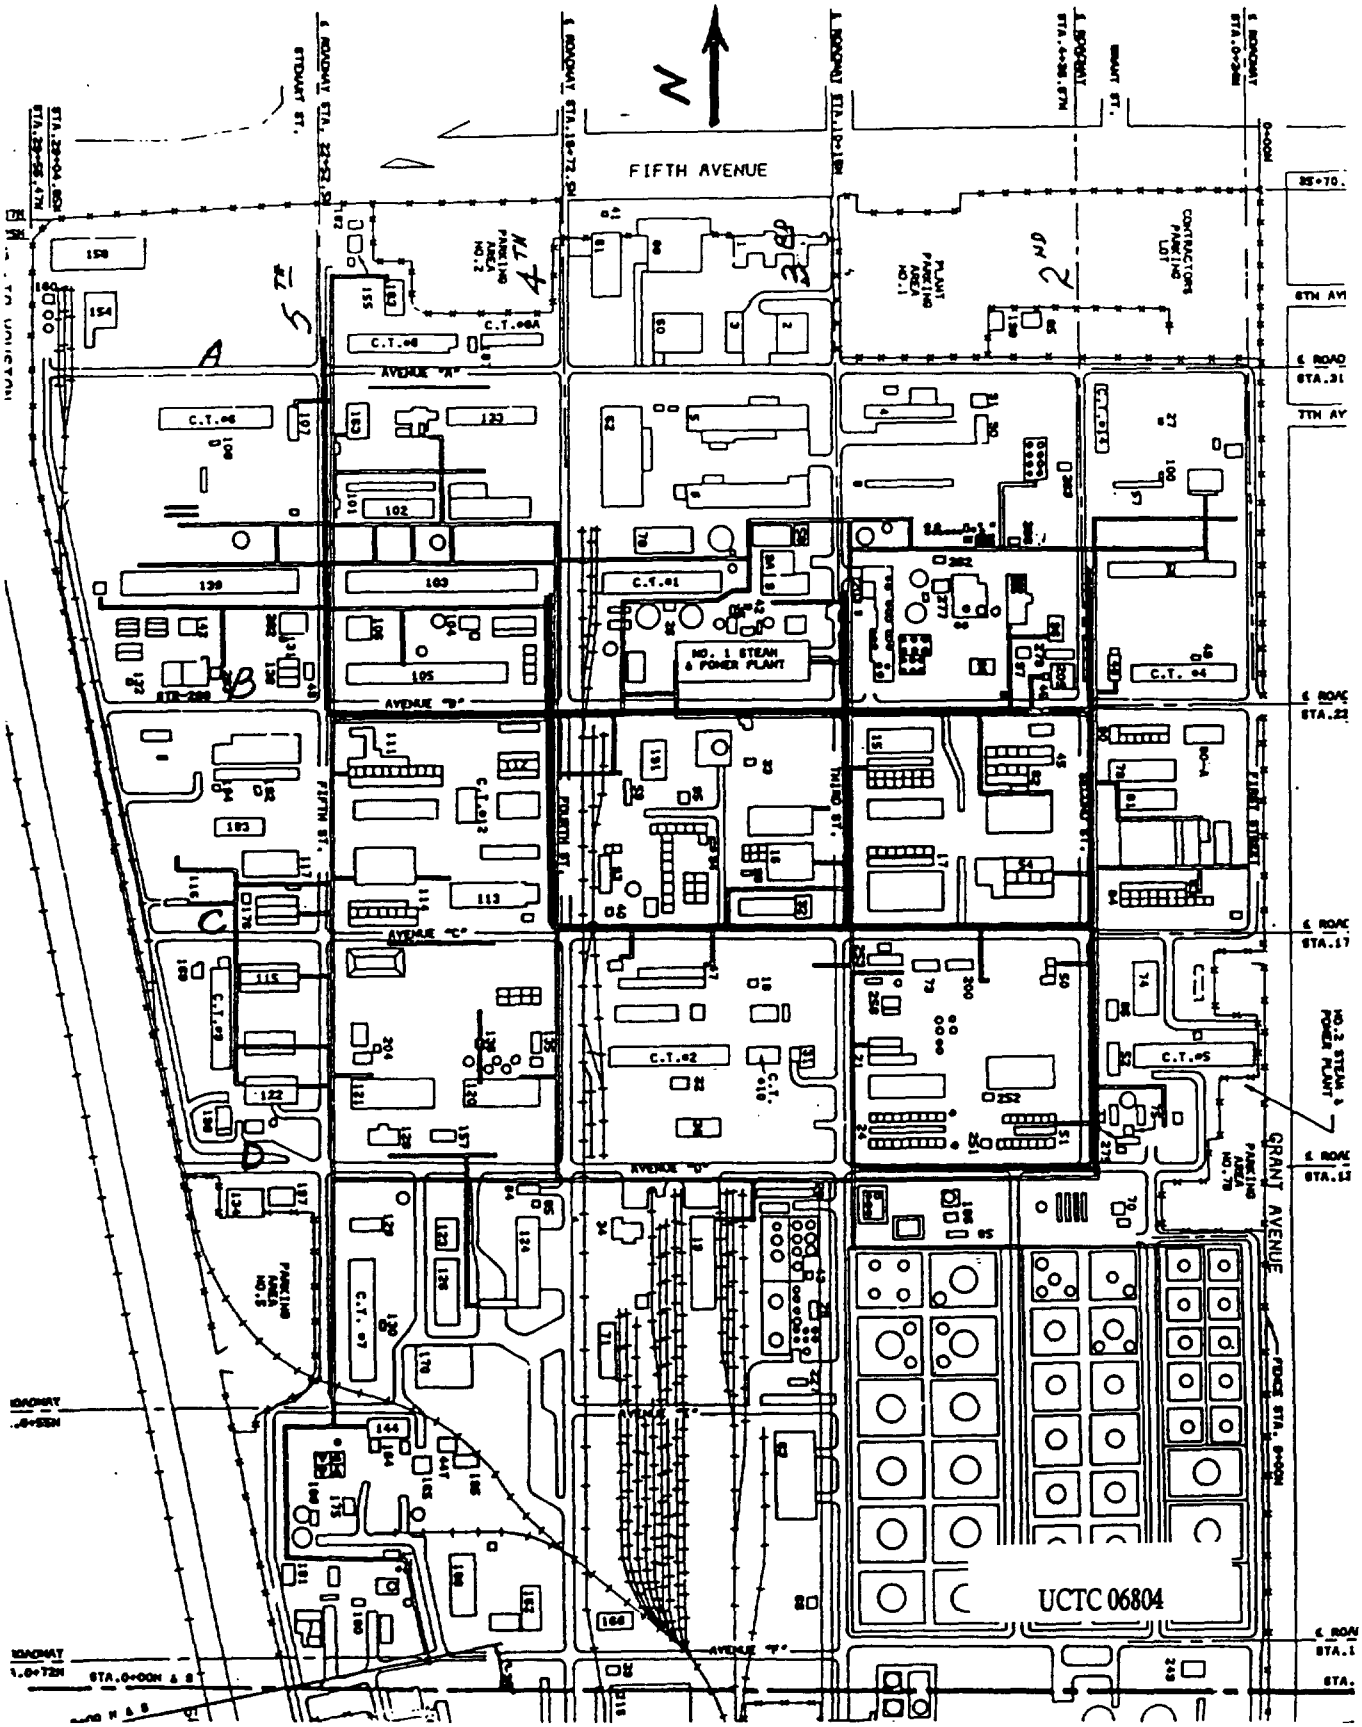

Published by AsbestosClaims.Law
asbestosclaims.law/library/16275/17

UNION CARBIDE INTERNAL CORRESPONDENCE

P. O. BOX 471, TEXAS CITY, TEXAS 77590

July 19, 1985

TO: P. D. Balmert
L. E. Calvert
S. J. Footer
R. W. Klein
R. A. Mendez
F. S. Provenzano
D. R. Reem

Gentlemen:

Attached is a copy of my memorandum "Plant Asbestos Project" for your comment and approval.

Very truly yours,

J. F. Schultz

UCTC 06787
