PLAINTIFF'S EXHIBIT
UC-3286

TECHNICAL CENTER SERVICES
UNION CARBIDE CORPORATION
CHEMICALS AND PLASTICS
SOUTH CHARLESTON, WEST VIRGINIA

RECEIVED
NOV 07 1978
G. F. HURLEY

MEMORANDUM

November 6, 1978

To: Mr. D. L. Brown ✓
Mr. E. Creech ✓
Mr. D. A. Dorsey ✓
Mr. N. B. Ellingwood ✓
Mr. W. H. Elliott ✓
Mr. R. W. Heatherly ✓
Mr. M. W. Jackson ✓
Mr. R. J. Jones ✓
Mr. W. T. Shelton ✓
Mr. C. W. Wible ✓

Copy: Mr. R. W. Blaine ✓
Mr. C. W. Carman ✓
Mr. D. H. Cook ✓
Mr. J. S. Garcia ✓
Mr. R. F. Hunt ✓
Mr. G. F. Hurley ✓
Mr. H. L. Roberts ✓
Mr. H. L. Robinson ✓
Mr. D. R. Shearer ✓

From: G. C. Merz/M. E. Perry

Subject: Demolition and Disposal of Asbestos Impregnated Insulation or Suspected Asbestos Impregnated Insulation - (Revised)

At the present time when we talk about demolition we mean any job no matter what size requiring removing of known or suspected insulation to do other work. To update and get further data on airborne material, Mr. Hurley's group will monitor all the demolition work until further notice.

The following job procedure must be used:

1. Notify Mr. Hurley's group when and where demolition will be. Do not start demolition until they have manned the job. Call one of the following:

G. F. Hurley	5129
M. W. Bosserman	5904
S. D. Herzog	5341

2. Prepare all surfaces to be demolished by wetting down, if possible. Follow any additional instructions from Mr. Hurley's group if needed.

UCC 000390

Union Carbide trial exhibit UC-3286: G. C. Merz and M. E. Perry on Demolition and Disposal of Asbestos Impregnat... Published by AsbestosClaims.Law
ACL Doc 18081 · Page 1 of 3 asbestosclaims.law/library/18081/1

3. Personal safety protection will be used during progression of job as recommended by the Safety Department or Environmental group.

4. All material contaminated with asbestos or suspected to be must be delivered (in plastic bags and properly tagged) to one of the following locations:

Disposal Shed No. 8722	For 770 Area
Disposal Shed No. 8723	For 701 Area
Disposal Shed No. 8736	For 740 Area

South West Corner of 781 for Rocket Hollow and 773 Area

(Note: This material will go to a landfill on a scheduled or when needed basis.)

5. Cleaning up area before leaving job is necessary.

6. No salvage material will be sent to salvage with insulation or known asbestos impregnation or suspected asbestos impregnation.

Would appreciate your cooperation in seeing that this is put into effect immediately.

Attached is a copy of proper tag to be attached to the bags. Tags may be obtained from W. T. Shelton, Building 704 or extension 5832.

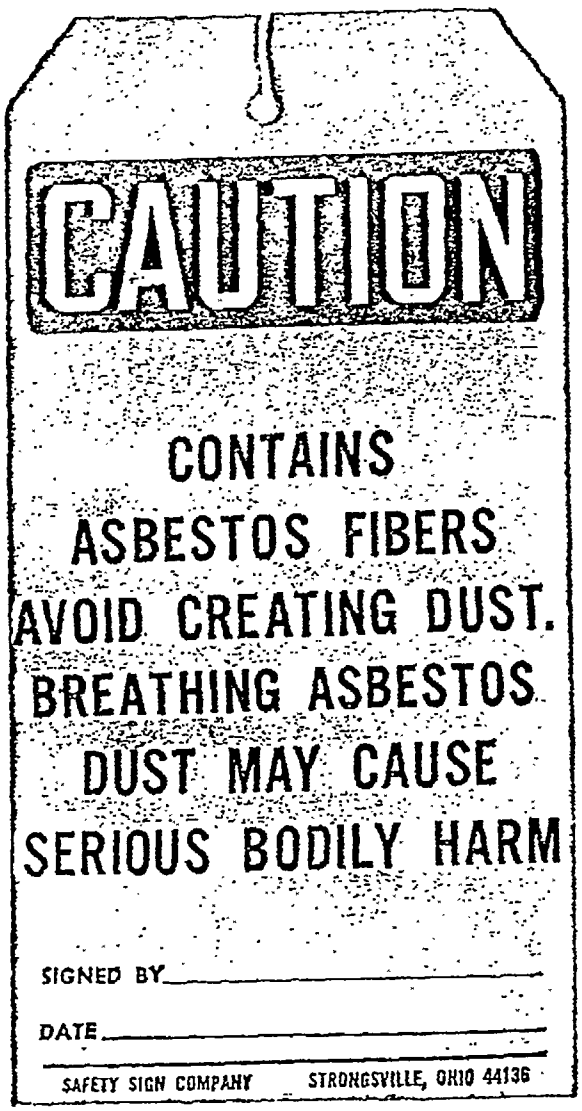
G. C. Merz

M. E. Perry

GCM:MEP:eem

Attachment

Union Carbide trial exhibit UC-3286: G. C. Merz and M. E. Perry on Demolition and Disposal of Asbestos Impregnat... Published by AsbestosClaims.Law
ACL Doc 18081 · Page 2 of 3 asbestosclaims.law/library/18081/2


CAUTION
CONTAINS
ASBESTOS FIBERS
AVOID CREATING DUST.
BREATHING ASBESTOS
DUST MAY CAUSE
SERIOUS BODILY HARM
SIGNED BY
DATE
SAFETY SIGN COMPANY
STRONGSVILLE, OHIO 44136

UCC 000392
